
MINNESOTA AVENUE NE REVITALIZATION

PHASE II

DCKA-2016-C-0040

FAP NO.: 2016 (006)

CONSTRUCTION MANAGER'S WEEKLY PROGRESS REPORT

09/18/2017 - 09/23/2017



Figure 1 Project VMS Board at Dix Street/Minnesota Avenue NE

PROJECT SUMMARY

Project Description


The work under this contract consists of the revitalization of Minnesota Avenue starting from 300 feet south of Benning Road, N.E. intersection to Sheriff Road, N.E. The project is approximately 0.90 mile in length. The project crosses Benning Road intersection, Watts Branch Bridge, and Nannie Helen Burroughs Intersection and it is located in Ward 7 in northeast Washington, DC (see Figure 1 for site map).

The planned work includes, the removal of existing surface asphalt and PCC road base, and the reconstruction of the pavement using full depth asphalt pavement.

It also includes;

- The total removal of existing sidewalks, existing curbs and gutters with the salvage and reuse of salvageable granite curbs. The demolished curb and gutter will be reconstructed using new granite curb and concrete gutter. Sidewalk will be replaced with new permeable concrete, PCC or Exposed Aggregate Sidewalk.
- New ADA compliant PCC wheelchair ramps.
- Reconstruction of PCC driveway entrances with and without exposed aggregate.
- Treatment and elimination of driveway entrances where required.
- New landscaping and streetscaping.
- Installation of bioretention facilities with plantings.
- Planting of new trees.
- Installation of new Water Quality catch basins to improve storm water runoff quality.
- Relocation of water main and service connections
- Replacing of existing fire hydrants with traffic-type breakaway fire hydrants.
- Installation of new permanent roadway signs and pavement markings.
- Installation of new street lights, conduits and wiring.
- Installation of new traffic signals, conduits and wiring.
- Installation of new underground electrical conduit as part of DC Plug.

The notice to proceed for the project was issued on September 11th, 2017 and project is scheduled to be completed by October 25th, 2019. Out of the total project days of 777 days, a total of six (6) days have been completed the project is left with a balance of 771days. There is currently no change order.

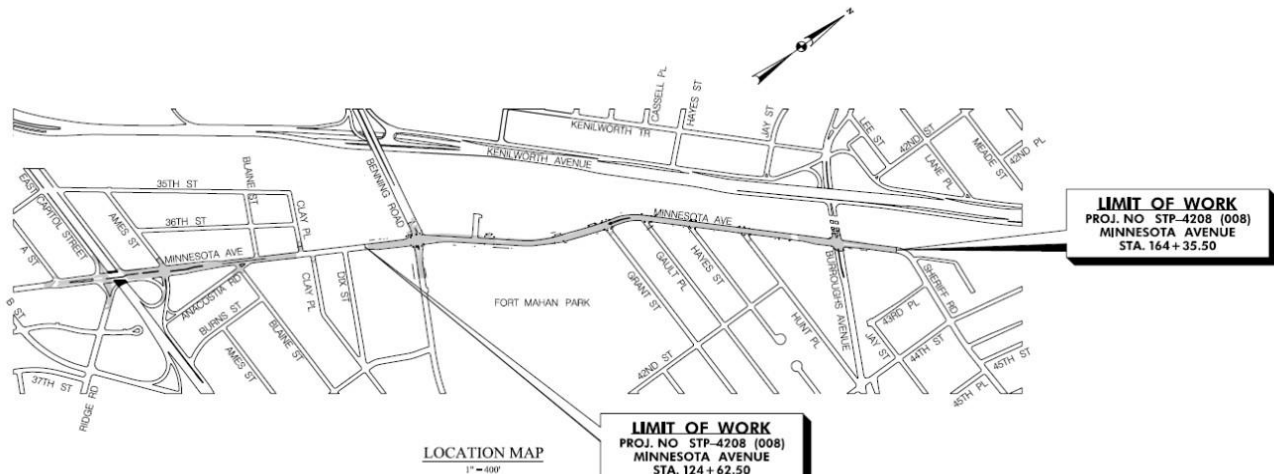

• Figure 2 Site Map

CONSTRUCTION PROGRESS

Summary of Work Performed:

The contractor started implementing the MOT plan by erecting temporary signs within project limits.

Field Office

Contractor is yet to provide the required field office, although effort is ongoing to acquire one.

ITEM 1

WORK PERFORMED FOR THE WEEK

1. Installation of temporary signs and supports.

ITEM 2

COMMUNITY OUTREACH

1. The project website www.minnesotaavenuephase2.com is online and updated with progress photos, two week look ahead and weekly reports to date.

ATTACHMENT A

PHOTOS OF WORK PERFORMED THIS PERIOD

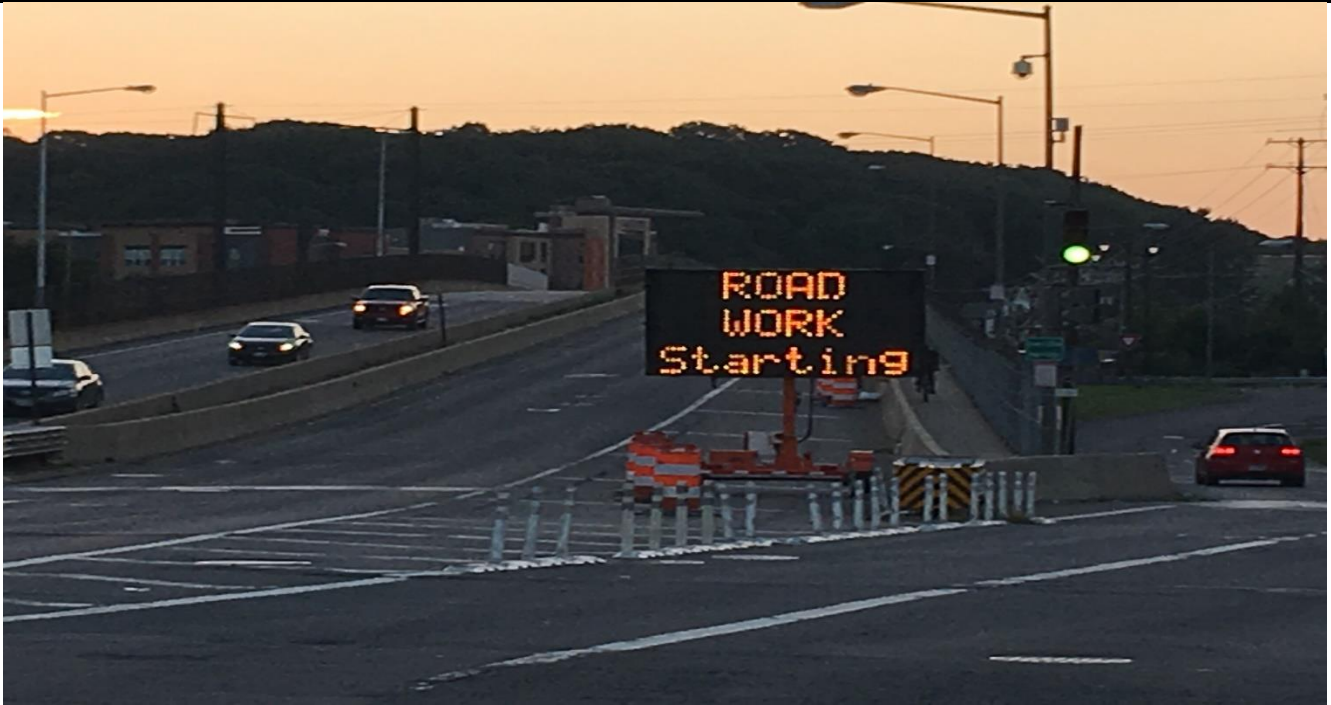


Figure 3 Project Sign Board Erected



• Figure 4 Through project limit at night to ensure VMS Board is working.
